



GALLAGHER

EST 1968



Construction Update – Thru November 8, 2016



Waxahachie ISD High School

Construction Update thru November 8, 2016



ADMINISTRATION:

Waxahachie Independent High School – Bldg and Site Package

Contact: Clyde Melick

ARCHITECTS:

Corgan Architects

401 North Houston Street, Dallas, Texas 75202

214-263-0660

Contact: David Safir

CONSTRUCTION MANAGER:

Gallagher Construction Services

3501 Token Drive, Ste 100, Richardson, Texas 75082

972-633-0564

Contact: Lance Aaron

OVERALL PROJECT STATUS

Current Activities:

- All concrete paving 85% complete.
- Water , Storm , Sanitary Sewer complete
- Drill piers to date 1,173. Only 160 left to drill.
- Grade beams Area "K" 100% Complete, Area "J" 95% Complete
- Continuing underground electrical site conduits
- MEP – Conduits and underground plumbing continuing at Area "K" and Area "B".

Two Week Look Ahead:


- Complete drill piers
- Complete grade beam at Area "J" and "H"
- Start grade beam forming at Area "N", "P" and "E"
- Complete site electrical conduit
- Complete all concrete parking lots and fire lane.
- Continue underground MEP at Building.



Grade beam forming continuing in "Area K" and Area "H". Wrecking forms of grade beams in "Area K". Starting to install MEP underground at "Area K".



Paving rebar installed at East Parking Lot in preparation of making pour. Concrete poured at South Loop Road. Liming Visitor parking lot at north main entry.

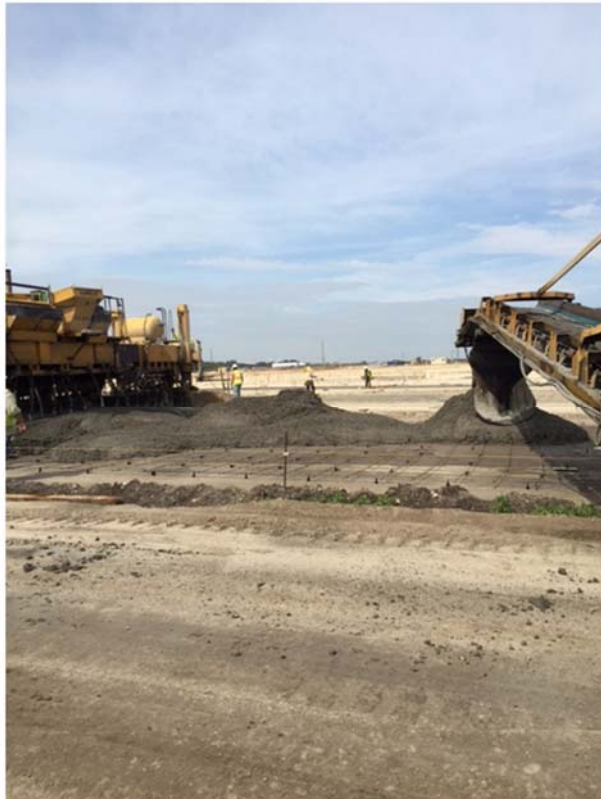

Paving pours at East Parking Lot and Loops Roads. Continuing to drill building piers - +/-1,100 piers drilled to date.

GALLAGHER CONSTRUCTION SERVICES
3501 TOKEN DR., SUITE 100, RICHARDSON, TX 75082
972.633.0564 • 972.633.0164 FAX
WWW.GALLAGHERTX.COM
