



GALLAGHER

EST 1968

Construction Update – Thru April 9, 2018



Waxahachie ISD High School

Construction Update thru April 9, 2018



ADMINISTRATION:

Waxahachie Independent High School – Bldg and Site Package
Contact: Clyde Melick

ARCHITECTS:

Corgan Architects
401 North Houston Street, Dallas, Texas 75202
214-263-0660
Contact: David Safir

CONSTRUCTION MANAGER:

Gallagher Construction Services
3501 Token Drive, Ste 100, Richardson, Texas 75082
972-633-0564
Contact: Lance Aaron

High School

Total Contract Sum	\$117,983,293
Total Completed To Date	\$ 94,500,622
Percent Complete	80%

Finley and Turner

Total Contract Sum	\$2,115,249
Total Completed To Date	\$ 2,099,464
Percent Complete	99%

OVERALL PROJECT STATUS

Current Activities:

- Greenhouse compete, working on MEP hookups
- Sidewalks ongoing at courtyard and around the building.
- Landscape and irrigation on-going
- Auditorium wood panels and sound panels being installed
- GFRC columns on-going
- All ceiling tile installed throughout the building
- Tile and flooring going down at the gym lobby and lecture hall
- Terrazzo going down in the gym and auditorium lobby
- Gym floors complete
- Turf going down at football field
- E layer going down at practice fields
- Foundation and fence posts being installed at baseball field.

Two Week Look Ahead:

- Final cleaning Area B 1st and 2nd floors
- Final Punch list complete at Area E and C
- Final punch remaining Area A,B and D
- Wood ceiling start in Area F
- Practice Sound Rooms being installed at Fine Arts
- Start Lecture Hall seating
- Cleaning and Sealing of athletic area floors start next week.
- Start sand and stain gym floors
- Wood Ceilings at Area P and K
- Turf at Football Field





CTE Culinary Kitchen,
Cosmetology and Beverage Area

Waxahachie ISD High School

Construction Update thru April 9, 2018



Band and Choir practice rooms being installed and band storage system installed.

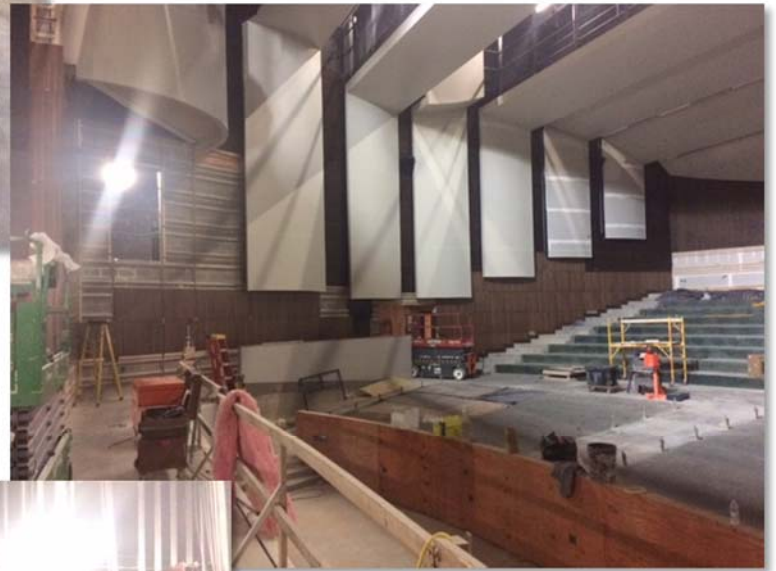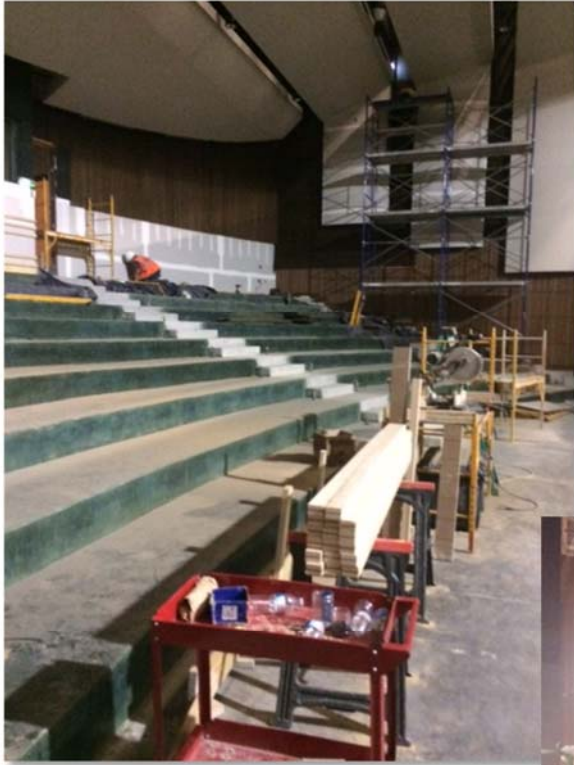

Auditorium finishes and stage rigging being installed.



30



Terrazzo at Auditorium Lobby, finished gym floors and lockers being installed.

Waxahachie ISD High School

Construction Update thru April 9, 2018



sg.



Tennis courts, band tower and football turf going down.

GALLAGHER CONSTRUCTION SERVICES
3501 TOKEN DR., SUITE 100, RICHARDSON, TX 75082
972.633.0564 • 972.633.0164 FAX
WWW.GALLAGHERTX.COM
