

Hopewell Valley Regional School District
 Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS
 FVHD # 4924D

Progress Report #12- 1/22/18 to 2/2/18

Exterior Site Work:

E1. Building "B" Addition: Underway
 Prep. for existing building storm drain piping.



E2. Building "B" Addition: Underway
 Remove existing fixtures (security camera, light, speaker, window AC unit) of existing exterior wall (cafeteria & Main office) to prep for new fire wall construction.




E3. Building "A" Addition: Underway
 Steel Erection "Phase 1" Columns & Beams



E4. Roof Work: Underway
 New gas line roughing to new water heater @ Performing Arts Mechanical Room, Roof top units ERU-G1 & ERU-G2 and from existing Boiler room to new Building "A" addition.



Hopewell Valley Regional School District
Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS
FVHD # 4924D





Interior Work:

- 1 Classroom #118: Underway
VCT floor installed- chase enclosure installed




- 2 300 Wing Toilets: Underway
Floor and wall ceramic tile, Plumbing fixture, Partitions, accessories, ceiling tiles and new LED light fixtures installation- Getting ready for final inspections.

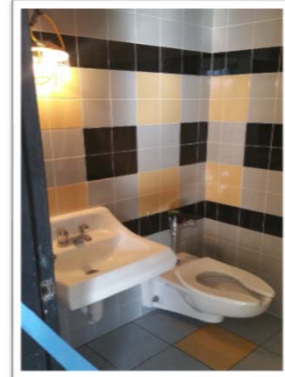

Hopewell Valley Regional School District
Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS
FVHD # 4924D

- 3 Classroom Swing #4 (313, 315 & 317): Underway
Remove existing ceiling tile, grid,
HVAC duct grills, light fixtures and
install new ceiling grid, tiles, grills and
LED light fixtures.



- 4 Ductless Heat Pump Units: Underway
All units at the 100 and 300 wing
classrooms installed except unites #
104A & 106A, Network cable pulled
for HP200 to HP227



- 5 Condensing Units: Underway
Network cable pulling for CU 2-3,
2-4 & 2-6
