

Hopewell Valley Regional School District  
 Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS  
 FVHD # 4924D

**Progress Report #10- 12/09/17 to 12/22/17**

Exterior Site Work:

E1. Building "B" Addition: Re- Underway  
 rout/ tie-in existing Building Storm  
 Water piping



E2. Building "B" Addition: Completed  
 Under slab Radon Mitigation/  
 Plumbing pipe installation, Concrete  
 slab preparations



E3. Building "B" Addition: Completed  
 Pouring concrete slab & depressed  
 areas



Hopewell Valley Regional School District  
 Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS  
 FVHD # 4924D

E4. Building "B" Addition: Underway  
 New Water line loop around new addition



E5. Dumpster Enclosure- Underway  
 Wall footings & Pad preparation.



E6. Building "A" Addition: Completed  
 Concrete Footing/ Piers, Anchor-bolt installation and foundation wall construction.




E7. Building "A" Addition: Underway  
 Under slab Bathrooms Plumbing pipe installation




Hopewell Valley Regional School District  
 Additions, Renovations & Rehabilitation Work at Hopewell Valley Central HS  
 FVHD # 4924D

Interior Work:

- 1 Classroom #118: Underway  
 Backfill under slab, poured concrete  
 and prep for VCT flooring installation.

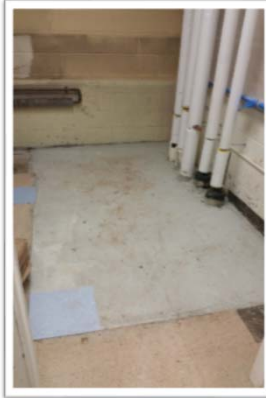

- 2 300 Wing Toilets: Underway  
 Remove existing fixtures, demolish  
 existing CMU chase wall, Cut existing  
 24" deep concrete slab to remove  
 imbedded existing fixture carriers-  
 exposed existing piping and start  
 roughing new piping

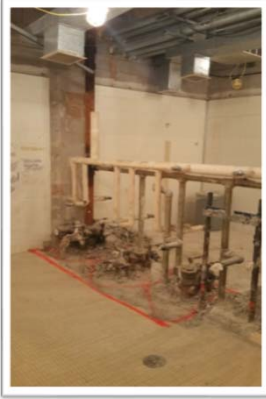

- 3 Classroom Swing #1 (323 & 325): Completed  
 Remove and replace existing ceiling  
 tile, grid, HVAC duct drops and grills

